Weibee Steel · Bid intelligence

Where we win, what it actually earns, and which of the next two years' opportunities deserve estimating hours.

413 bids from Jan 2022 to Sep 2026 · 107 jobs · 36 general contractors · 90 pipeline opportunities · generated 2026-10-11 00:27

Findings Hit rate Customers Estimate vs actual Pricing feedback Capacity Bid / no-bid Trusting the odds Glossary

How to read this page in two minutes

1. **The six numbers at the top** say how the business is doing right now: how often we win, what we won, how full the shop is, and how much margin we keep.
2. **Findings** are the seven things the data says, each with a next action. If you read nothing else, read these.
3. **The charts** show where the numbers come from. Hover over any bar or line for the detail.
4. **The bid / no-bid scorecard** is the decision tool: every upcoming project ranked, with a Pursue / Review / Pass call and the reasons in plain words.
5. **The last section** says how much to trust the win odds. Short version: good enough to rank, not good enough to overrule the room on one job.

Words like *hit rate*, *gross margin* and *win odds* are explained in the glossary at the bottom.

Work sample on synthetic data. Every number here comes from a seeded, generated bid history built to look like a mid-size Oklahoma fabricator-erector. Nothing is Weibee Steel's data. The pipeline, the marts and the scorecard logic are what would run on the real thing; see the README for what the intake would need to capture.

25%
Hit rate, trailing 12 months
20 of 80 decided bids; prior year 33%

$19.4M
Value won, trailing 12 months
5,088 tons

16 weeks
Won work waiting for the shop
2,286 tons at 140 tons a week

50%
How full the shop looks, next 12 months
won work plus upcoming work counted at its win odds

4.5 pts
Margin we estimated but did not keep
estimated 22.9%, actually earned 18.3%

29 of 90
Upcoming projects worth chasing
about 698 estimating hours to bid them all

Findings

Computed from the marts, not typed in. Each has a next action.

1. **Where the shop fits.** K-12 school, Church / worship, Retail / commercial win 37%-41% of decided bids and give back 3.0 pts or less of estimated margin. Sports / recreation, Hospitality, Multifamily podium win 12%-15% and give back 7.4-10.4 pts. Together the bottom three consumed 29% of estimating hours for 18% of dollars won.

   → Default the bottom three to Review in the bid/no-bid meeting; bid them only with a relationship GC or a negotiated scope.

2. **Pricing feedback.** When we lose on price and get a number back (100 of 161 price losses), our bid is a median 9.7% above the low bid. On hard bids the hit rate is 20% against an average of 5.6 bidders; negotiated work wins 49%. When we win and learn the next number, we left a median 3.9% on the table.

   → Collect the low number on every loss (coverage is 62% today); a gap under 3 % is a markup conversation, a gap over 10 % is a fit conversation.

3. **Price shoppers.** 7 general contractors (Ouachita Building Group, Pioneer Civic Builders, Osage Builders, Heartland Build Co...) have awarded us 18% of bids with a median price gap of 10.7%: 2,650 estimating hours for $19.1M won. The 4 A-class accounts returned $29.4M on 1,920 hours.

   → Bid price-shopper invitations only when the shop needs fill-in work; spend the hours on A-class GCs and on new accounts that look like them.

4. **Geography.** Hit rate falls from 39% inside 60 miles to 22% beyond 250 (23 bids). Field hours on far jobs ran 25% over estimate.

   → Treat erection work beyond 250 miles as fab-only unless the GC is a relationship account; price per-diem crews explicitly when we do erect.

5. **Capacity and pipeline coverage.** Won work still to fabricate is 2,286 tons, 16 weeks at 140 tons/week. Adding the probability-weighted pipeline, projected utilisation over the next four quarters is 2026Q3 77%, 2026Q4 66%, 2027Q1 49%, 2027Q2 46%, 2027Q3 35%. 4 of those quarters sit below 70 %.

   → The 29 Pursue opportunities carry 9,872 tons at 39% average win odds; to fill the open quarters the pipeline needs roughly 9,393 more tons of identified opportunities at today's hit rate.

6. **Estimated versus actual.** Across 95 completed jobs we estimated 22.9% gross margin and realised 18.3%: 4.5 pts, about $4.3M of margin. Shop hours ran 10% over estimate and field hours 8%; complexity 5 work slipped most (10.6 pts).

   → Feed realised margin by project type and complexity back into the estimate as a line-item contingency instead of a flat markup.


7. **How much to trust the win odds.** Out-of-time test on 100 bids after 2025-07-01: AUC 0.75, Brier 0.182 against 0.206 for always guessing the base rate. The model separates good bets from bad ones; it does not call individual bids. Use it to rank and to budget estimating hours, not to skip a job the room believes in.

   → Re-fit quarterly; the model gets better with every decided bid and every low-bid number we collect.

Hit rate: where we win


Decided bids only. The dashed line is the overall hit rate; what matters is the spread around it and the dollars won per estimating hour.

Hit rate by quarter

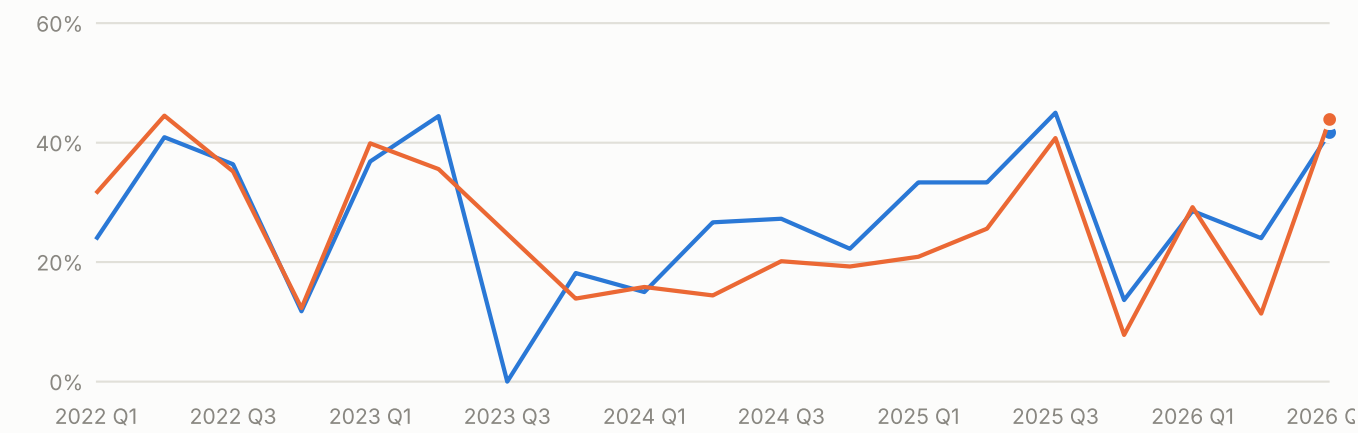


Count and dollar hit rates on decided bids (won + lost). Cancelled projects are excluded.


By project type

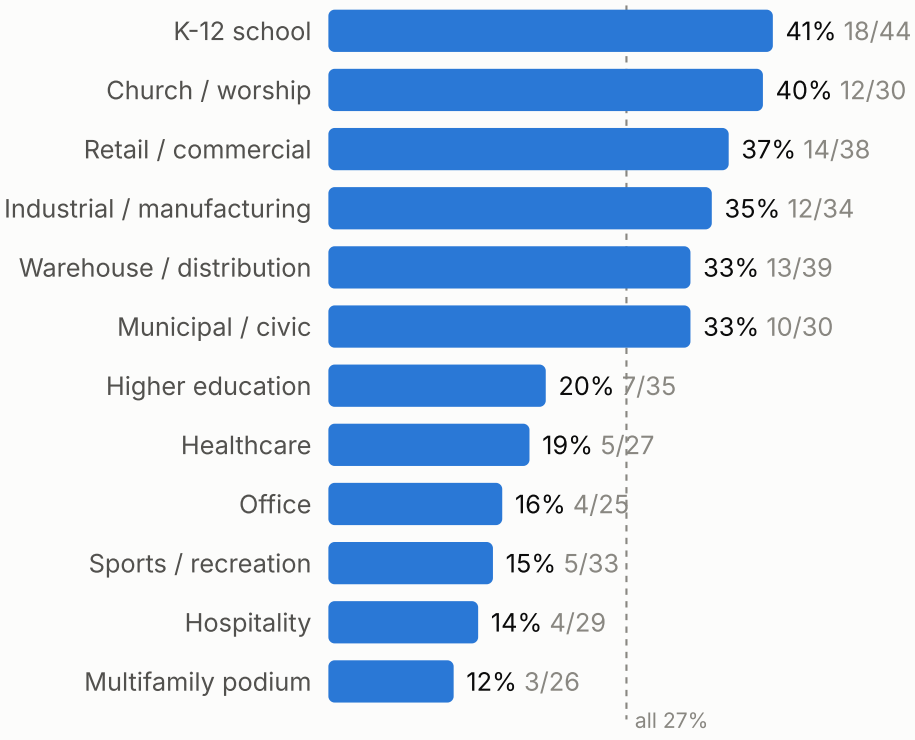


By size

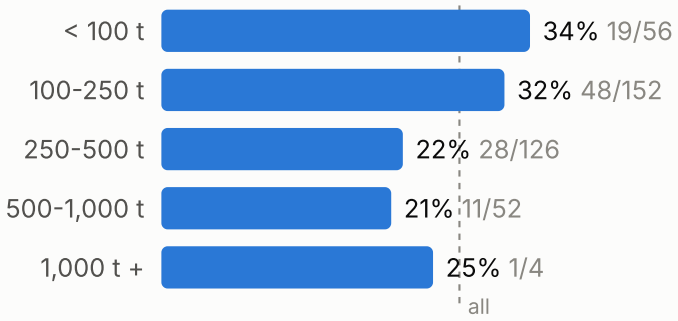


By distance from the shop

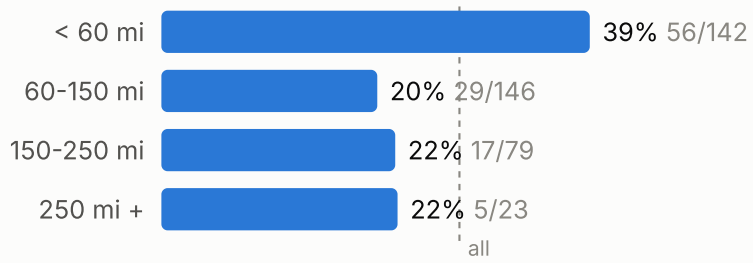

By delivery method

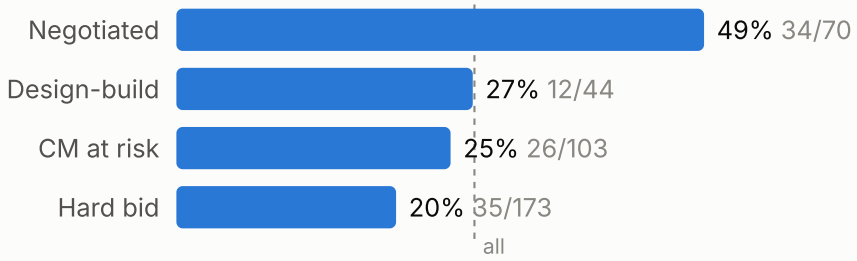

Dollars won per estimating hour, by project type

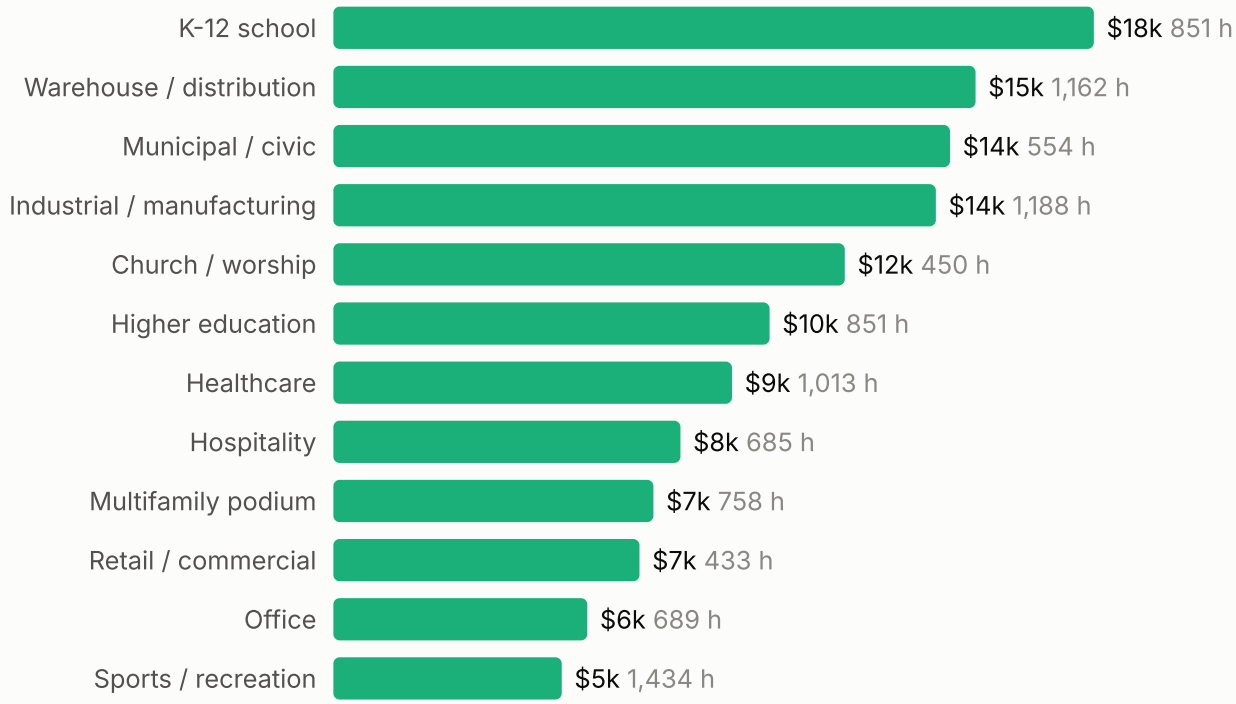

Estimating hours are the scarce input; this is the return on them.

Customers: who awards us, and what the work is worth

Hit rate alone flatters GCs who send us everything; realised margin, change-order behaviour and payment speed belong next to it.

Customer scorecard

General contractor	Tier	Class	Bids	Hit rate	Won	Won / est. hr	Median price gap	Realised n
Sooner State Contractors	regional	A	20	45%	$11.8M	$18k	12.0%	17%
Granite Peak Builders	regional	A	24	42%	$8.4M	$14k	9.5%	20%
Wagon Trail Builders	national	A	19	53%	$8.0M	$16k	11.9%	23%
Ouachita Building Group	regional	B	17	24%	$6.8M	$13k	9.7%	15%
Meridian Build Partners	regional	B	23	30%	$6.5M	$12k	9.8%	18%
Washita Valley Builders	local	C	17	18%	$6.3M	$15k	8.4%	16%
Longhorn Commercial	regional	B	9	33%	$6.1M	$21k	5.6%	28%

General contractor	Tier	Class	Bids	Hit rate	Won	Won / est. hr	Median price gap	Realised n
Great Plains Constructors	national	B	18	33%	$5.6M	$12k	9.7%	23%
Red River Builders	regional	B	19	32%	$5.5M	$12k	8.4%	20%
Verdigris Construction	local	B	9	56%	$4.8M	$20k	-	15%
Panhandle Constructors	regional	B	5	40%	$4.6M	$21k	12.4%	16%
Pioneer Civic Builders	local	C	13	15%	$3.3M	$10k	11.2%	4%
Osage Builders	regional	B	16	25%	$3.1M	$8k	10.8%	19%
Summit Ridge Construction	national	B	17	29%	$2.9M	$8k	8.6%	23%
Trinity Basin Builders	regional	B	9	33%	$2.9M	$16k	4.1%	15%
Heartland Build Co	local	C	11	18%	$2.4M	$7k	11.1%	14%
North Fork General Contractors	local	B	10	30%	$2.2M	$13k	13.6%	13%
Cimarron Commercial	regional	B	8	38%	$2.2M	$16k	8.6%	18%
Blue Stem Contracting	regional	B	11	36%	$1.8M	$9k	7.9%	21%
Ironhorse Contractors	national	C	14	21%	$1.8M	$5k	10.5%	14%
Flint Hills Construction	local	B	6	33%	$1.7M	$12k	10.0%	15%
Sandstone General	local	C	11	18%	$1.4M	$5k	6.8%	13%
Cross Timbers Contracting	regional	B	4	25%	$1.3M	$21k	9.0%	26%
Cedar Creek Commercial	national	A	4	50%	$1.2M	$7k	-	25%
Canadian River Construction	local	C	20	10%	$938k	$2k	9.6%	17%
Boomer Construction Group	local	C	7	14%	$719k	$3k	10.7%	19%
Prairie Wind General	local	New / thin	2	50%	$410k	$16k	-	21%


General contractor	Tier	Class	Bids	Hit rate	Won	Won / est. hr	Median price gap	Realised n
Crossroads Construction	regional	C	16	6%	$393k	$782	8.9%	23%
Timberline GC	regional	C	5	20%	$101k	$1k	10.2%	22%
Keystone Commercial Builders	local	C	6	0%	-	-	8.7%	-
Arbuckle Builders	local	New / thin	2	0%	-	-	9.8%	-
Lone Elm Construction	regional	C	3	0%	-	-	-	-
Caddo Construction	local	C	3	0%	-	-	9.5%	-
Cottonwood General Contractors	national	C	3	0%	-	-	-	-
Tallgrass Construction	local	C	5	0%	-	-	10.9%	-
Mesa Vista Construction	local	C	4	0%	-	-	9.1%	-

A = awards us ≥ 40 % and executes at or above shop margin; B = awards ≥ 22 %; C = below. Sorted by value won. The class is a starting point for account planning, not a verdict.

Estimate vs actual: what the work really earns


The estimate is a forecast. Comparing it to the job's final numbers, by type and complexity, is the feedback loop that makes the next estimate better.

Estimated vs realised gross margin, by project type

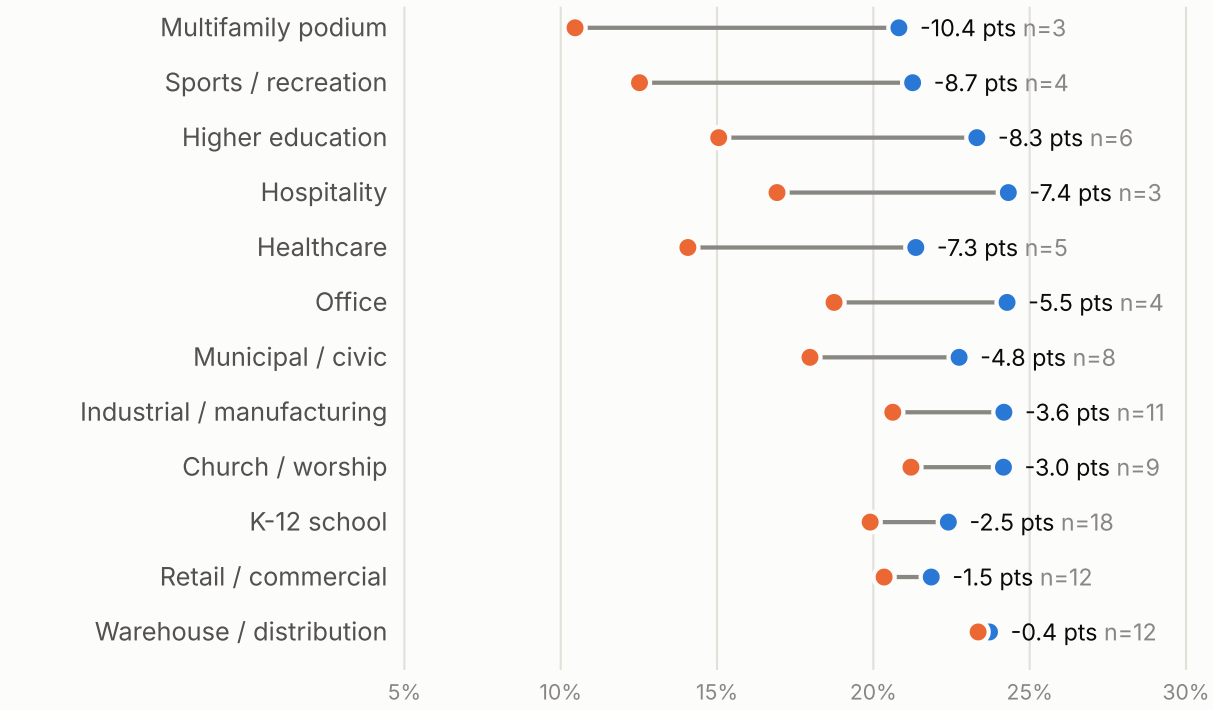


Dollar-weighted over completed jobs. Gross margin is before overhead.

By complexity

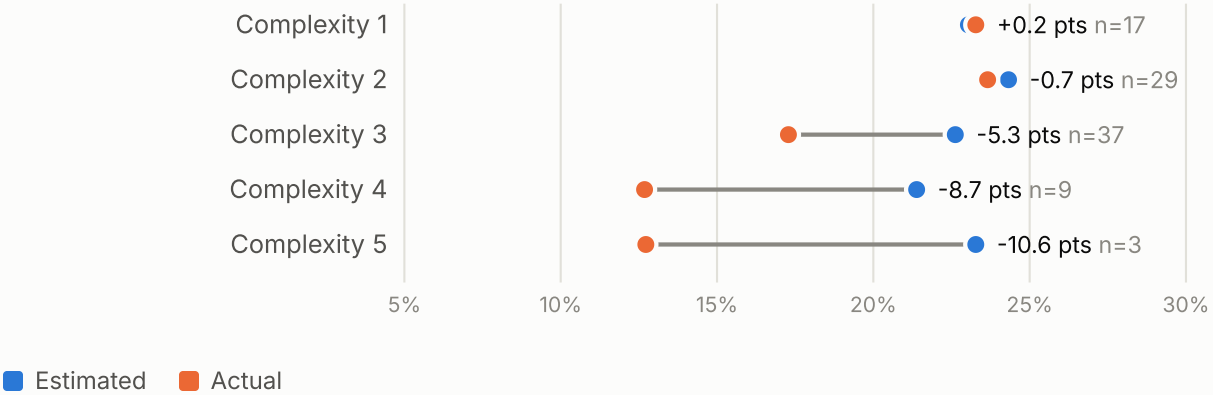

1 = simple braced frames, 5 = AESS, long span, heavy moment connections.

Field-hour overrun by project type

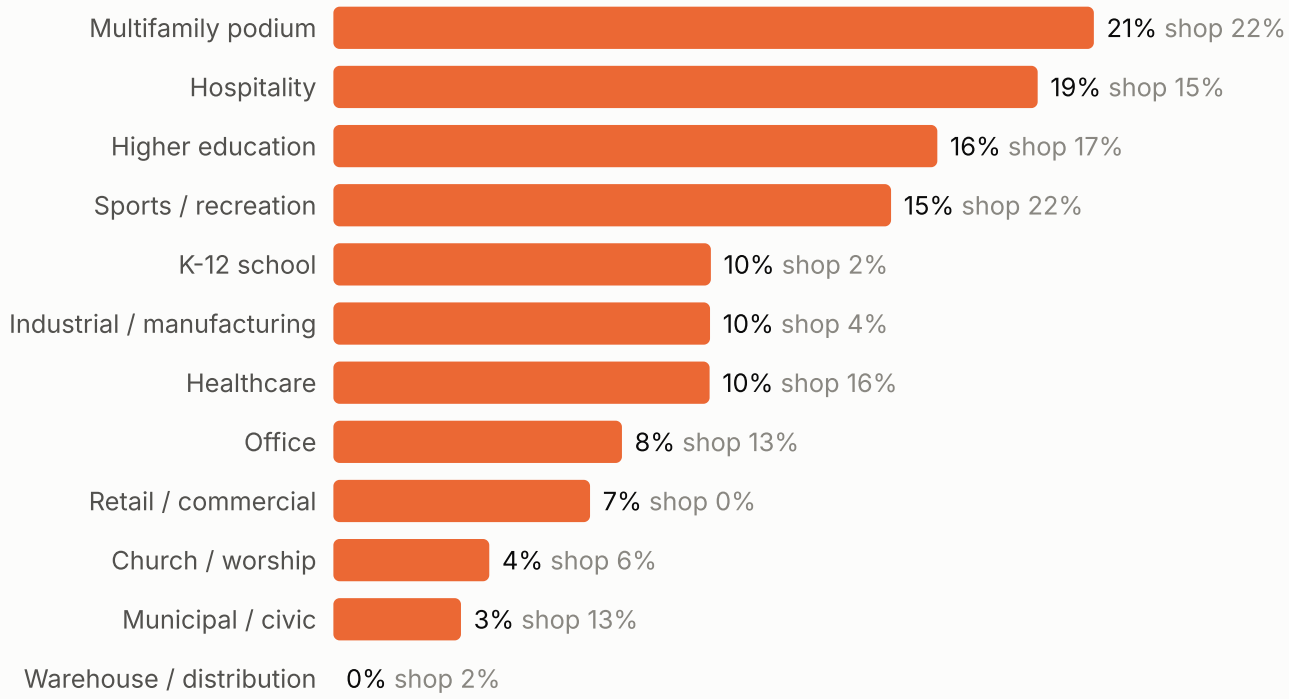


Positive = more hours than estimated. Shop variance in the note.

Pricing feedback: how far off were we?

Collected from GCs after award. The distribution says whether a loss is a markup problem or a fit problem.

How far above the low bid were we when we lost on price?

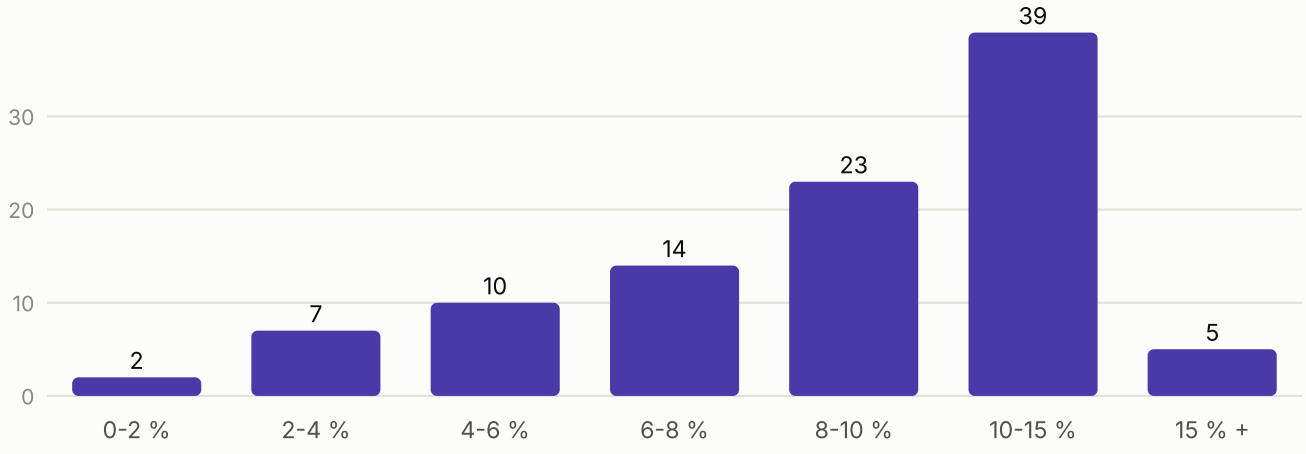

Lost-on-price bids where the GC shared the low number.


Median price gap by delivery method



Capacity: can the shop take what we are chasing?

Won work spread over fabrication windows, plus pipeline opportunities weighted by their win odds, against shop capacity.

Shop load: backlog and probability-weighted pipeline vs capacity, tons per week

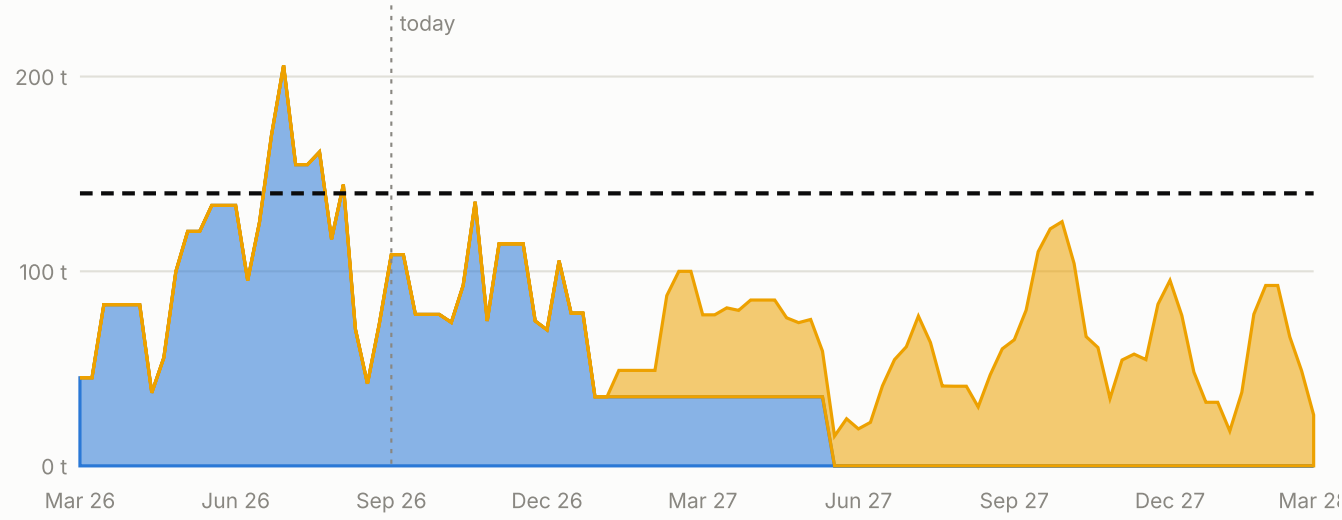

Each won job spreads its tonnage evenly over its fabrication window; each pipeline opportunity contributes tons × win probability over its expected window.

By quarter

Quarter	Backlog t/wk	Weighted pipeline t/wk	Projected utilisation
2026Q3	108	0	77%
2026Q4	93	0	66%
2027Q1	47	21	49%
2027Q2	27	37	46%
2027Q3	0	50	35%

Quarter	Backlog t/wk	Weighted pipeline t/wk	Projected utilisation
2027Q4	0	81	58%
2028Q1	0	54	39%

Bid / no-bid scorecard

Every upcoming opportunity scored on win odds, realised margin, estimating cost, shop load and fit. A starting point for the weekly bid meeting; the room overrides it with judgement and the override is logged.

Summary

Call	Opportunities	Estimating hours	Tons	Expected margin $ net of estimating
Pursue	29	698	9,872	$2.5M
Review	26	451	4,608	$718k
Pass	35	859	9,961	$529k

Ranked opportunities (next 6-24 months)

#	Call	Project	GC	Type
1	Pursue	Industrial - Stillwater #24	Caddo Construction	Industrial / manufacturi
2	Pursue	Municipal - Norman #23	Flint Hills Construction	Municipal / civic
3	Pursue	Industrial - Muskogee #3	Meridian Build Partners	Industrial / manufacturi
4	Pursue	Industrial - Oklahoma City #11	Boomer Construction Group	Industrial / manufacturi
5	Pursue	K-12 school - Tulsa #26	Sooner State Contractors	K-12 school
6	Pursue	Industrial - Oklahoma City #45	Summit Ridge Construction	Industrial / manufacturi
7	Pursue	Municipal - Tulsa #61	Meridian Build Partners	Municipal / civic
8	Review	Municipal - Muskogee #32	Cimarron Commercial	Municipal / civic
9	Pursue	Industrial - Stillwater #49	Flint Hills Construction	Industrial / manufacturi
10	Pursue	Industrial - Moore #30	Washita Valley Builders	Industrial / manufacturi
11	Pursue	Warehouse - Broken Arrow #48	Heartland Build Co	Warehouse / distributio

#	Call	Project	GC	Type
12	Pursue	Industrial - Edmond #87	Meridian Build Partners	Industrial / manufacturi
13	Pursue	Healthcare - Norman #51	Cross Timbers Contracting	Healthcare
14	Pursue	Industrial - Oklahoma City #41	Washita Valley Builders	Industrial / manufacturi
15	Pursue	Church - Oklahoma City #63	Trinity Basin Builders	Church / worship
16	Pursue	Warehouse - Tulsa #12	Osage Builders	Warehouse / distributio
17	Review	K-12 school - Durant #25	Osage Builders	K-12 school
18	Pursue	Office - Tulsa #57	Summit Ridge Construction	Office
19	Pursue	K-12 school - Broken Arrow #35	Ironhorse Contractors	K-12 school
20	Pursue	Warehouse - Shawnee #38	Wagon Trail Builders	Warehouse / distributio
21	Pursue	K-12 school - Fort Smith #42	Sooner State Contractors	K-12 school
22	Pursue	Sports - Norman #85	Heartland Build Co	Sports / recreation
23	Pursue	Warehouse - Edmond #67	Heartland Build Co	Warehouse / distributio
24	Pursue	Healthcare - Oklahoma City #19	Timberline GC	Healthcare
25	Pursue	Retail - Norman #71	Wagon Trail Builders	Retail / commercial
26	Pursue	K-12 school - Ardmore #86	Osage Builders	K-12 school
27	Pursue	Church - Norman #59	Red River Builders	Church / worship
28	Pursue	K-12 school - Edmond #75	Sooner State Contractors	K-12 school
29	Pursue	K-12 school - Broken Arrow #13	Granite Peak Builders	K-12 school
30	Pursue	Retail - Tulsa #6	Cross Timbers Contracting	Retail / commercial
31	Pursue	Higher education - Wichita #20	Heartland Build Co	Higher education
32	Review	Church - Enid #65	Granite Peak Builders	Church / worship
33	Review	Church - Oklahoma City #14	Granite Peak Builders	Church / worship

#	Call	Project	GC	Type
34	Review	Warehouse - Sherman #4	Ouachita Building Group	Warehouse / distributio
35	Review	Warehouse - Oklahoma City #79	Osage Builders	Warehouse / distributio
36	Review	Church - Little Rock #76	Ironhorse Contractors	Church / worship
37	Review	Sports - Moore #1	North Fork General Contractors	Sports / recreation
38	Review	Office - Broken Arrow #84	Summit Ridge Construction	Office
39	Review	Retail - Ardmore #52	Great Plains Constructors	Retail / commercial
40	Review	Church - Norman #37	Sooner State Contractors	Church / worship
41	Review	Municipal - Stillwater #88	Caddo Construction	Municipal / civic
42	Pass	Retail - Norman #64	Canadian River Construction	Retail / commercial
43	Review	Retail - Tulsa #55	Blue Stem Contracting	Retail / commercial
44	Review	Office - Norman #16	Red River Builders	Office
45	Review	Municipal - Tulsa #78	Washita Valley Builders	Municipal / civic
46	Review	K-12 school - Tulsa #18	Osage Builders	K-12 school
47	Pass	Warehouse - Fort Smith #83	Longhorn Commercial	Warehouse / distributio
48	Review	Warehouse - Oklahoma City #81	Osage Builders	Warehouse / distributio
49	Review	Warehouse - Little Rock #22	Ironhorse Contractors	Warehouse / distributio
50	Pass	Healthcare - Norman #21	Cross Timbers Contracting	Healthcare
51	Review	Sports - Tulsa #17	Sooner State Contractors	Sports / recreation
52	Review	Office - Tulsa #82	Blue Stem Contracting	Office
53	Review	Sports - Norman #60	Sandstone General	Sports / recreation
54	Review	Multifamily podium - Oklahoma City #29	Pioneer Civic Builders	Multifamily podium
55	Review	Retail - Oklahoma City #89	Caddo Construction	Retail / commercial
56	Review	K-12 school - Oklahoma City #7	Wagon Trail Builders	K-12 school
57	Pass	Industrial - Fort Worth #47	Cedar Creek Commercial	Industrial / manufacturi

#	Call	Project	GC	Type
58	Review	K-12 school - Amarillo #62	Canadian River Construction	K-12 school
59	Review	Office - Oklahoma City #72	Boomer Construction Group	Office
60	Pass	Healthcare - Dallas #36	Canadian River Construction	Healthcare
61	Pass	Office - Kansas City #73	Summit Ridge Construction	Office
62	Pass	Retail - Wichita #44	Timberline GC	Retail / commercial
63	Pass	Municipal - Kansas City #69	Arbuckle Builders	Municipal / civic
64	Pass	Multifamily podium - Norman #40	Pioneer Civic Builders	Multifamily podium
65	Pass	Office - Edmond #53	Washita Valley Builders	Office
66	Pass	Municipal - Fayetteville #58	Ironhorse Contractors	Municipal / civic
67	Pass	Sports - Moore #43	Summit Ridge Construction	Sports / recreation
68	Pass	Church - Joplin #90	Red River Builders	Church / worship
69	Pass	Multifamily podium - Enid #68	Washita Valley Builders	Multifamily podium
70	Pass	Municipal - Fort Worth #8	Meridian Build Partners	Municipal / civic
71	Pass	Warehouse - Wichita #9	Timberline GC	Warehouse / distributio
72	Pass	Healthcare - Oklahoma City #15	Arbuckle Builders	Healthcare
73	Pass	Sports - Sherman #54	Sandstone General	Sports / recreation
74	Pass	Higher education - Little Rock #5	Pioneer Civic Builders	Higher education
75	Pass	Warehouse - Lubbock #27	Tallgrass Construction	Warehouse / distributio
76	Pass	Higher education - Fort Worth #70	Canadian River Construction	Higher education
77	Pass	Office - Stillwater #10	Crossroads Construction	Office
78	Pass	Higher education - Austin #74	Ouachita Building Group	Higher education
79	Pass	Sports - Denton #80	Crossroads Construction	Sports / recreation


#	Call	Project	GC	Type
80	Pass	Higher education - Enid #2	Cedar Creek Commercial	Higher education
81	Pass	K-12 school - Joplin #33	Cimarron Commercial	K-12 school
82	Pass	Sports - Edmond #56	Sooner State Contractors	Sports / recreation
83	Pass	Office - Tulsa #39	Heartland Build Co	Office
84	Pass	Multifamily podium - Muskogee #77	Red River Builders	Multifamily podium
85	Pass	Hospitality - Dallas #50	Canadian River Construction	Hospitality
86	Pass	Higher education - Stillwater #31	Washita Valley Builders	Higher education
87	Pass	Multifamily podium - Wichita Falls #46	Red River Builders	Multifamily podium
88	Pass	Multifamily podium - Shawnee #34	Ouachita Building Group	Multifamily podium
89	Pass	Healthcare - Joplin #66	Great Plains Constructors	Healthcare
90	Pass	Higher education - Lubbock #28	Pioneer Civic Builders	Higher education

EV = win odds × expected revenue × margin we actually realise on that project type, minus estimating cost. EV per estimating hour is ranked against what an hour has returned historically (Pursue ≥ 80 %, Review ≥ 35 %). Shop load = backlog + the rest of the pipeline weighted by its odds + this job in full, averaged over its fabrication window.

Model card


A regularised logistic regression on our own bid history, evaluated out of time. Small, interpretable, re-fit quarterly.

What moves the win odds

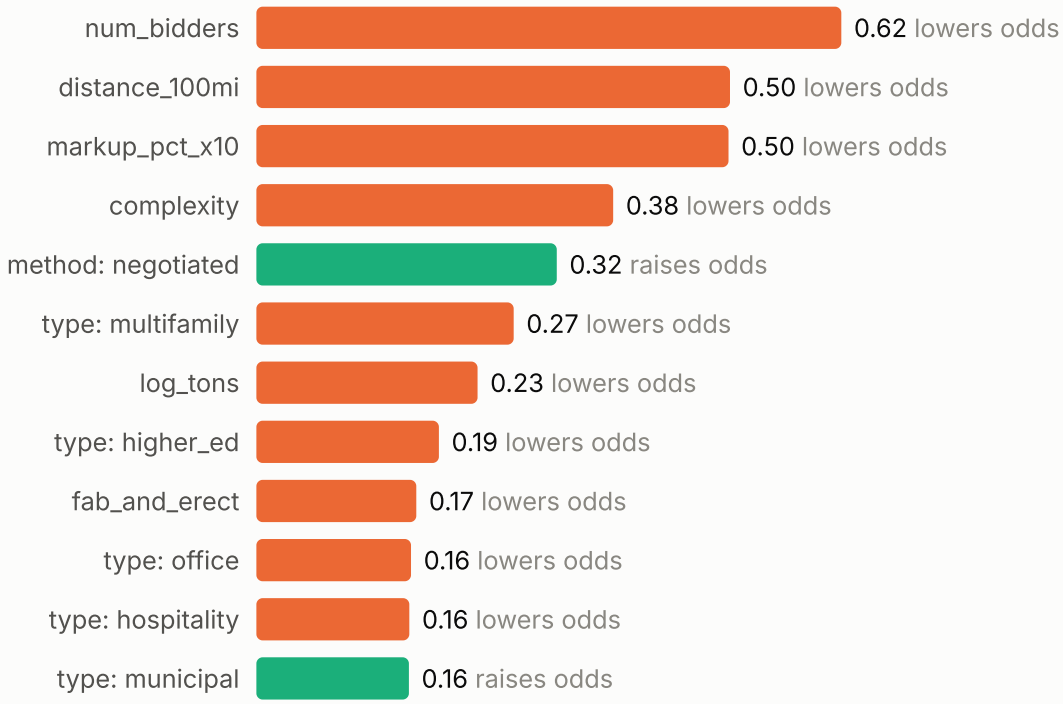

Standardised logistic-regression coefficients; reference levels are warehouse work and hard bid. Green raises the odds, orange lowers them.

Calibration on held-out bids

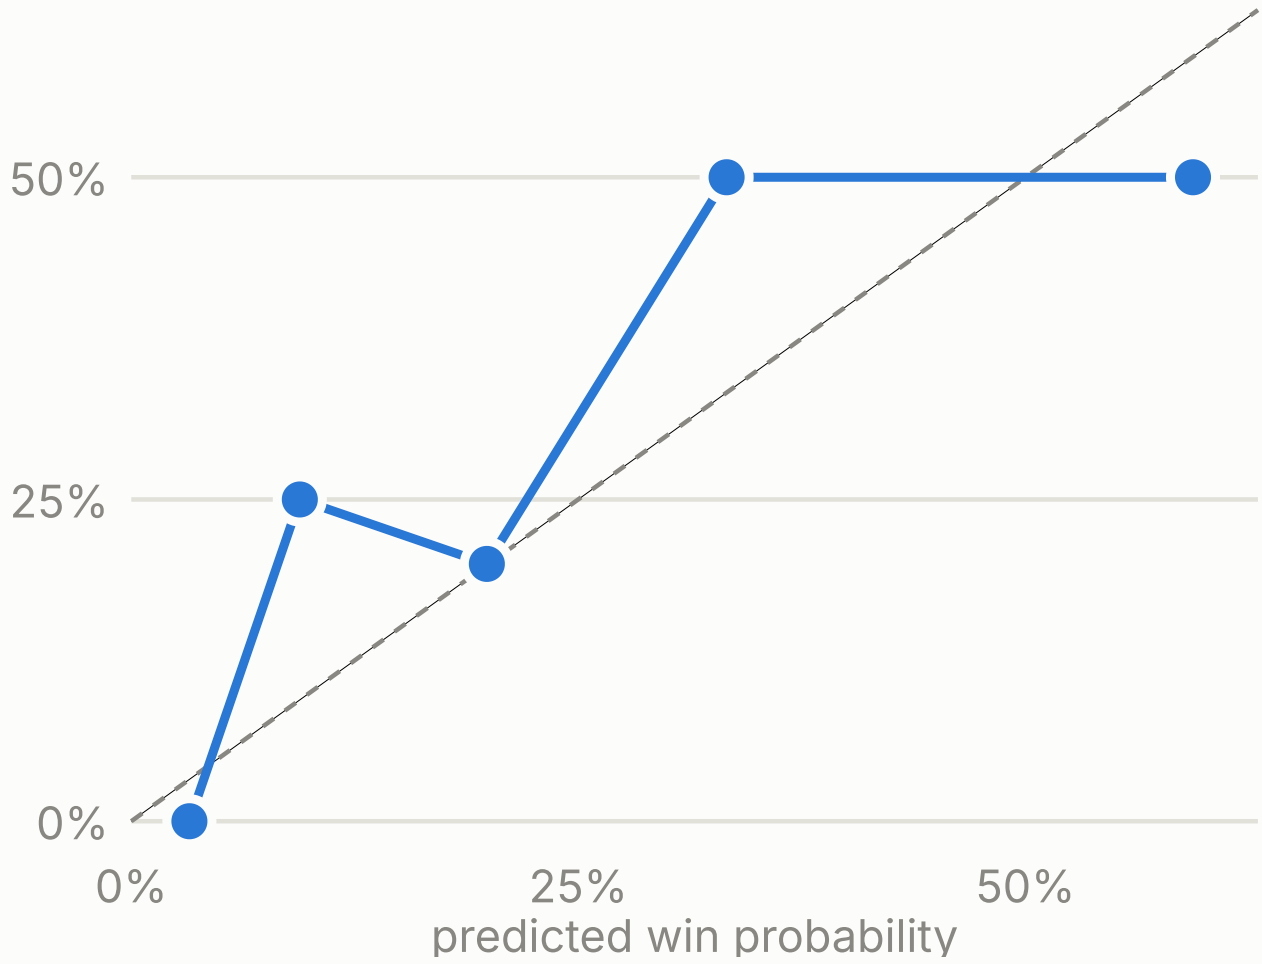

Split	Bids	Base rate	AUC	Brier	Brier, base-rate guess	Log loss	Log loss, base-rate guess
train	290	27%	0.80	0.151	0.197	0.465	0.582
test	100	29%	0.75	0.182	0.206	0.537	0.603

Trained on bids before 2025-07-01, tested on the ones after. Points near the diagonal mean a 30 % call wins about 30 % of the time.

Built with Python, DuckDB and plain SVG. Pipeline: synthetic history → DuckDB marts (SQL) → win model → scorecard → this page.
